

FINAL PRE-ROLLOUT AUDIT

SandPro OMP production readiness

objectivetracker.net · observed production · August 4, 2026

DECISION: HOLD the unguarded company-wide launch

Proceed tomorrow only as a controlled, staffed rollout after the hard gates in this report are cleared or explicitly accepted by accountable owners. The application is visually strong and core surfaces function after hydration; adoption, first-load truth, communication freshness, and operational data stewardship are not yet company-wide ready.

5 / 90

PERSONNEL EVER SIGNED IN
85 have never signed in

~7.4s

FALSE-ZERO NCR WINDOW
Measured at mobile viewport

74

OPEN NCRS
48 critical · 45 past due

Aug 1

CURRENT PRODUCTION
DEPLOY
Vercel READY

WHAT IS READY

Core desktop and responsive mobile surfaces render cleanly and the Create flow opens without a write.
Dashboard, OKR, KPI, NCR, Organization, Admin groups, account settings, and Fix-It all hydrate with production data.
Production deployment is READY; no Vercel error or warning log entries were returned for the last 24 hours.
Relevant public tables have RLS enabled; Fix-It has 0 active and 28 archived items.

WHAT IS NOT READY

Company-wide authentication and onboarding: only 5 SandPro personnel have ever signed in.
First-load truth: several routes display credible zero/empty states for 5–8 seconds before real data appears.
Rollout communication: the auto-open Daily bulletin still announces Wednesday, June 24 as the company-wide launch.
NCR operating ownership: 73 of 74 open NCRs have no owner and none are ready for closeout.
Real-employee, ordinary-role, installed-PWA, inbox/junk, and device-push proof remains unobserved in this audit.

01 / DECISION

The decision and the minimum safe path

This is not a recommendation to cancel adoption. It is a recommendation to change the launch shape until the evidence matches the promise.

Recommended launch posture

NO-GO for an unguarded all-company launch in which 90 employees are expected to self-activate and operate independently.
CONDITIONAL GO for a controlled, staffed, department-by-department activation wave after the seven hard gates below are green or formally risk-accepted.

Seven hard gates before the first broad cohort

STATE	GATE	ACCEPTANCE EVIDENCE
RED	Daily bulletin	Replace or retire the June 24 rollout story; verify a fresh bulletin in production.
RED	Activation	Named owner, credential path, and successful sign-in proof for every first-wave user.
RED	Ordinary-role proof	Validate a real employee/member account across visibility, Create, notifications, and org surfaces.
RED	First-load truth	Use an explicit loading state or brief every facilitator never to treat early zeros as final data.
RED	Device / channel proof	One actual employee device: install/launch PWA, enable push, receive a push, receive email, inspect junk.
AMBER	Security acceptance	Close or formally accept exposed SECURITY DEFINER execute grants and leaked-password protection risk.
AMBER	NCR operating posture	Name the accountable triage owner and communicate that the historical backlog is not launch-day work.

What would make tomorrow safe

Start with 5–10 employees, not all 90. Hold the next wave until every person signs in and completes the same short checklist.
Keep one launch commander, one activation lead, one product/support lead, and one NCR/data steward in the room or on call.
Treat login failure, wrong data visibility, false zeros lasting more than 15 seconds, or notification delivery failure as stop-the-line events.
Pause the next cohort; do not attempt a data rollback. Preserve the working pilot group while the issue is diagnosed.

02 / SCOPE

What was audited — and what was deliberately not changed

Evidence is limited to observed production, authoritative read-only data, and read-only deployment/platform inspection.

Surfaces inspected

SURFACE	IDENTITY / VIEWPORT	OBSERVED
Entry + Daily	Release Smoke Admin · desktop	Auto-open bulletin, current date, stale rollout story
Tasks & Projects	Desktop + 390×844	KPI cards, list, filters, ownerless-NCR banner
Create	Desktop + 390×844	Wizard opened; no record submitted
OKR	Desktop + 390×844	90-line August check-in view; four company OKRs visible
KPI Command Center	Desktop	Computed objectives/NCR lens; manual scorecard empty
NCR	Desktop + 390×844	Tracker, Closeout, Analytics, KPA Import, Dept triage
Organization + Admin	Desktop + 390×844	97-person org, users, 10 assignment groups
Notifications + account	Desktop	Empty personal feed; push enable setting; profile menu
Fix-It	Desktop	0 active / 28 archived after hydration

Authoritative checks

- Supabase project whgrkfhuzgwmbelocnhq: read-only SQL, table counts, auth cohort, notification coverage, NCR completeness, RLS presence, security and performance advisors.
- Vercel deployment inspection: production alias, deployment ID, READY state, build region/runtime, cron configuration, recent error/warning query.
- Live HTTP/PWA inspection: response headers, manifest, service worker, cache strategy, icons/shortcuts declarations.
- Repository provenance check: current HEAD and dirty-worktree state only; no build, test, migration, commit, deploy, or cleanup was run.

Audit boundary

No production records were edited, no forms were submitted, no imports or exports were triggered, no notifications were sent, no users were invited or changed, and no Fix-It items were archived. This was not a physical-device test and did not prove any employee mailbox, Microsoft 365 trace, or installed-PWA session.

03 / PRODUCTION TRUTH

The current production snapshot

All figures below are current observed values from August 4, 2026, not targets or presentation estimates.

97 AUTH USERS / PROFILES 96 confirmed	92 OBJECTIVES 82 active · 10 complete	370 NCR RECORDS 296 closed · 74 open	1,810 NOTIFICATIONS Historical records
--	--	---	---

Deployment and runtime

ITEM	OBSERVED PRODUCTION VALUE	ASSESSMENT
Primary URL	https://objectivetracker.net	READY
Vercel deployment	dpl_BxFsSyqh7V5TsM89uHqBJWkAy8V	READY
Deployment created	Aug 1, 2026 · 4:24:41 PM CDT	3 days old
Runtime	Vite static app + Node 24.x serverless functions	Observed
Crons	Daily digest 13:00 UTC weekdays; reminders 14:00 UTC daily	Configured
Local repository HEAD	6b0bbe9 · keep OKR headers visible · Jul 29	Not proven live
Deploy-to-commit linkage	No Git commit metadata returned by Vercel inspection	Traceability gap

Production controls that are already healthy

- RLS is enabled on relevant public data tables inspected in production.
- Vercel returned no production error or warning log entries in the last 24-hour query window.
- The sampled last 100 auth events contained 99 informational events and one transient 500 ('context canceled') during the audit.
- The Fix-It queue is operationally clean: 0 active, 28 archived.
- All 92 objectives have owners; none are marked blocked.
- Ten active assignment groups exist, including All Personnel and Office Personnel.

04 / ADOPTION

Activation is the true company-wide blocker

The accounts exist. The usage evidence does not.

Activation is the dominant rollout constraint

90 SandPro personnel accounts · 7 support / QA accounts excluded



Only 1 of 90 personnel signed in during the last seven days.

Production auth cohort. Support and QA identities are excluded from the 90-person SandPro population.

COHORT	TOTAL	EVER SIGNED IN	NEVER SIGNED IN	LAST 7 DAYS
All auth users	97	11	86	5
SandPro personnel	90	5	85	1
Support / QA	7	6	1	4

Department exposure

DEPARTMENT	EVER / TOTAL	ROLLOUT IMPLICATION
Field	0 / 39	Largest cohort has no prior sign-in proof.
Wellhead Shop	0 / 10	No sign-in proof.
CP Warehouse	0 / 9	No sign-in proof.
Flowback Shop	0 / 7	No sign-in proof.
Automation	1 / 6	One prior user; five unproven.
Sales	1 / 5	One prior user; four unproven.
Admin	1 / 4	Admin coverage is thin.
Leadership	1 / 2	One of two proven.
Quality	1 / 3	One of three proven.

Important interpretation

97 accounts and 96 confirmed addresses do not equal 90 rollout-ready employees. A password hash proves account provisioning, not that the employee knows the credential, can reset it, can see the right data, or can complete work on their actual device.

Activation script for each wave

- Sign in as the employee — not an admin or QA account.
- Open Tasks & Projects and wait for hydrated counts; confirm the employee sees only intended work.
- Open one objective, OKR, NCR, Organization, and Fix-It surface.
- Open Create, select a type, and stop before submission unless the rollout script calls for a real record.
- Install or launch the PWA on the actual device; enable push only with the employee present.
- Receive one email and one push, then confirm the notification opens the intended record.

05 / FIRST-LOAD TRUTH

Believable zeros appear before real data

This is the most dangerous product-behavior issue because it looks like valid business truth, not a loading state.

Measured behavior

On a 390×844 mobile viewport, NCR displayed zero cards and 0 of 0 records for more than five seconds; the real 74 / 45 / 48 / 296 counts appeared at approximately 7.36 seconds. Dashboard, OKR, KPI, Organization, and Fix-It showed the same false-empty pattern during this audit, generally resolving within 5–10 seconds.

OKR · false empty

OMP

Tasks & ProjectsOKRNCROrganization

NewAdd to OKRRelease Smoke Admin

OKR

OKR LINE · 2026STATUSYTD AVGCADENCEDEPARTMENTAUDIT FORMBASELINETARGETJANFEBMARAPRMAJJUN

No OKRs yet. Add a main OKR to get started.

OKR · hydrated

OMP

Tasks & ProjectsOKRNCROrganization

NewAdd to OKRRelease Smoke Admin

OKR

OKR LINE · 2026STATUSYTD AVGCADENCEDEPARTMENTAUDIT FORMBASELINETARGETJANFEBMARAPRMAJJUN

Aug 0 of 30 lines updated — 30 left open

CEMENTARY 4 lines

2.0 Digital Operating System

On Track23.3MonthlyCompanyYNot ActiveFULL ACTIVE10152

Employee Cost of under 27%

At Risk25.9MonthlyCompanyN36%+27%38413

Greater Net Profit of 15%

At Risk5.8MonthlyCompanyN10%10%6-121

Zero TRR

On Track0MonthlyCompanyN000001

CP WAREHOUSE 5 lines

CP Shared Client SM- idle time.

On Track0MonthlyCP WarehouseNDefine what success...1-1

CP Warehouse asset throughput per day.

On Track2.4MonthlyCP WarehouseNDefine what success...1-1

Create baseline

On Track24.4MonthlyCP WarehouseYDefine what success...1-1

Decreasing the number of Events

On Track2.9MonthlyCP WarehouseYDefine what success...1-1

Meeting 100% of client stock level

On Track2.9MonthlyCP WarehouseYDefine what success...1-1

Top (5) Routers - Time start to time

KPI · false zero

OMP

Tasks & ProjectsOKRNCROrganization

NewAdd to OKRRelease Smoke Admin

SANDPRO EXECUTION SYSTEM

KPI Command Center

Goal-linked operating KPIs from live objectives and NCRs. OKRs and manual scorecards appear when they have real source data.

This quarterAll KPIsAll departmentsRefresh

OPERATING HEALTH

No data

0 action KPIs · 0 watch KPIs · 5 missing data KPIs · 0 measured of 5

ACTIVE OBJECTIVES

0

0 blocked or flagged · internal dev rows excluded

NCR CLOSURE

0%

0 open · 0 critical · 0 unclassified

MANUAL SCORECARDS

No data

0 datapoints scored

COMPANY OPERATING KPIs

Quarterly execution lens

7-day due readiness

0 objectives

Target 0 objectives · Live

No active objectives are available for due-readiness yet.

No active objectives are available for due-readiness yet.

QUALITY / NCR

NCR closure rate

0%

Target 85%

No NCR records are available in this lens.

No NCR records are available in this lens.

DETAIL LENS

7-day due readiness

0 objectives

Target 0 objectives · Live

No active objectives are available for due-readiness yet.

7-day due readiness has no current datapoint. Add a manual value or import a CSV before relying on this KPI.

Definition

Active objectives due in the next seven days.

KPI · hydrated

OMP

Tasks & ProjectsOKRNCROrganization

NewAdd to OKRRelease Smoke Admin

SANDPRO EXECUTION SYSTEM

KPI Command Center

Goal-linked operating KPIs from live objectives and NCRs. OKRs and manual scorecards appear when they have real source data.

This quarterAll KPIsAll departmentsRefresh

OPERATING HEALTH

75%

0 action KPIs · 1 watch KPIs · 1 missing data KPI · 4 measured of 5

ACTIVE OBJECTIVES

82

0 blocked or flagged · internal dev rows excluded

NCR CLOSURE

80%

74 open · 48 critical · 3 unclassified

MANUAL SCORECARDS

No data

0 datapoints scored

COMPANY OPERATING KPIs

Quarterly execution lens

7-day due readiness

0 objectives

Target 0 objectives · Live

No active objectives are available for due-readiness yet.

No active objectives are available for due-readiness yet.

QUALITY / NCR

NCR closure rate

80%

Target 85%

74 NCRs open; 48 critical, 23 non-critical, 3 Manual Scorecards unclassified, 40%

DETAIL LENS

7-day due readiness

0 objectives

Target 0 objectives · Live

No active objectives are available for due-readiness yet.

7-day due readiness is inside the target band. Keep the current operating rhythm and watch freshness.

Definition

Active objectives due in the next seven days.

OKR TRUST

State key results

0 KRrs

Target 0 KRrs

No key results are configured in this lens yet.

No key results are configured in this lens yet.

Mobile NCR · 5.5 sec

OMP

NCR

+Add to OKRRelease Smoke Admin

NCR Tracker

Non-conformance reports, root causes, corrective actions, and assigned follow-up work.

+ New NCR

Take / add photo or doc to NCR

Tracker

Closeout Report

Analytics

KPA Import

OPEN

0

Click to filter

PAST DUE

0

Click to filter

DUE 7 DAYS

0

Click to filter

CRITICAL OPEN

0

Click to filter

CLOSED

Mobile NCR · 7.4 sec

OMP

NCR

+Add to OKRRelease Smoke Admin

NCR Tracker

Non-conformance reports, root causes, corrective actions, and assigned follow-up work.

+ New NCR

Take / add photo or doc to NCR

Tracker

Closeout Report

Analytics

KPA Import

Dept triage (194)

OPEN

74

Click to filter

PAST DUE

45

Click to filter

DUE 7 DAYS

0

Click to filter

CRITICAL OPEN

48

Click to filter

CLOSED

Before-and-after production evidence. The left states are not screenshots taken too early by accident; they are the user-visible truth until hydration completes.

Why this matters tomorrow

A new user may conclude the app is empty, broken, or that their permissions are wrong.

A leader may read 0 open NCRs or 0 active objectives as actual operating status.

The state can trigger refreshes, duplicate support tickets, and unnecessary sign-outs during onboarding.

Route-by-route settling creates inconsistent screenshots and makes facilitator troubleshooting harder.

Safe temporary operating instruction


Until the interface has explicit loading semantics

Facilitators should wait 10 seconds after every first route open. If data remains at zero after 15 seconds, hard-refresh once, then stop the cohort and escalate. Do not make a management decision from a first-load zero.

06 / COMMUNICATION

The auto-open Daily bulletin is stale on launch eve

The first message shown to a user contradicts the August 5 rollout schedule.

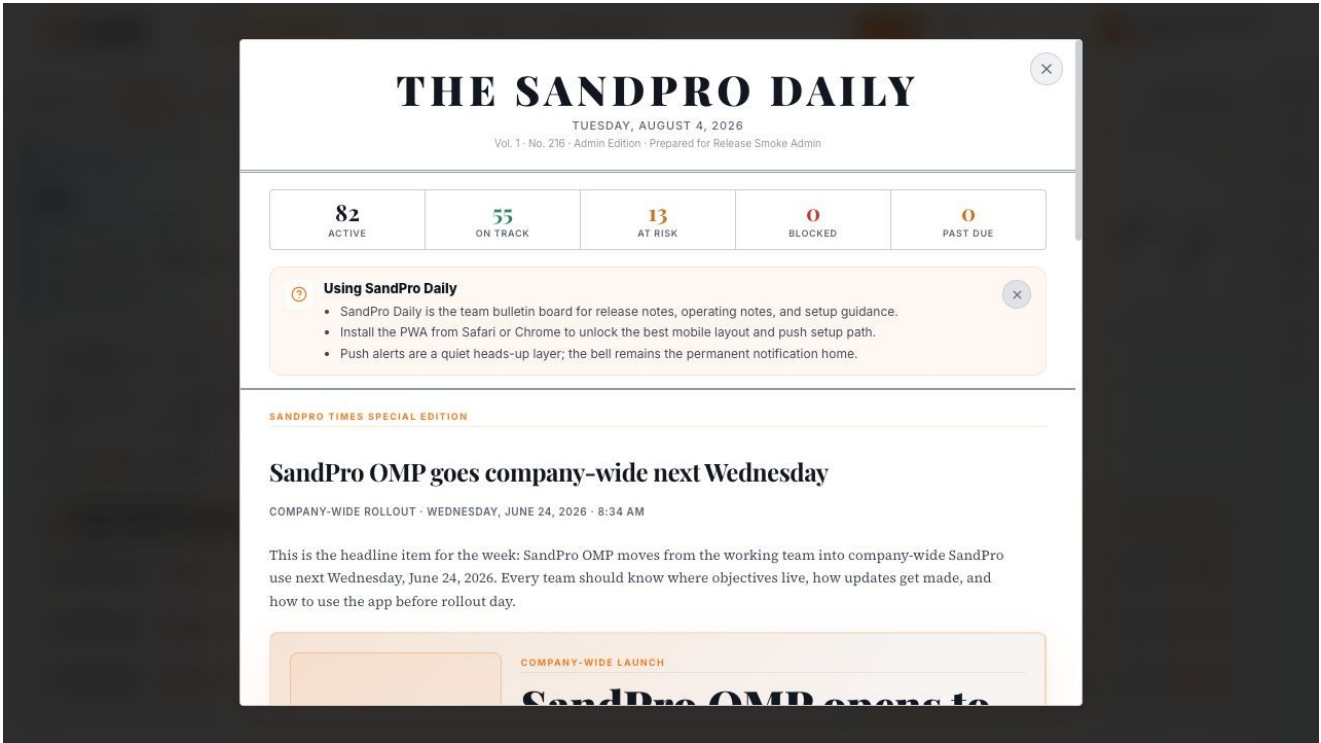

Observed on entry August 4, 2026: current-day masthead with a rollout story dated Wednesday, June 24, 2026.

Observed conflict

ELEMENT	OBSERVED TEXT	RISK
Current masthead	Tuesday, Aug 4, 2026	Current
Headline	SandPro OMP goes company-wide next Wednesday	Misleading
Article date	Wednesday, June 24, 2026 · 8:34 AM	Stale
Body	Moves company-wide next Wednesday, June 24	Contradictory


Gate

A stale auto-open rollout announcement is a trust failure at the exact moment new users are deciding whether the system is current. Refresh it, clearly label it as archive, or suppress it before the first broad cohort — then reopen production and prove the corrected state.

07 / OBJECTIVES + OKR

The execution system works, but deadline and KPI semantics need care

The objective portfolio is populated and owned; most work has no due date.

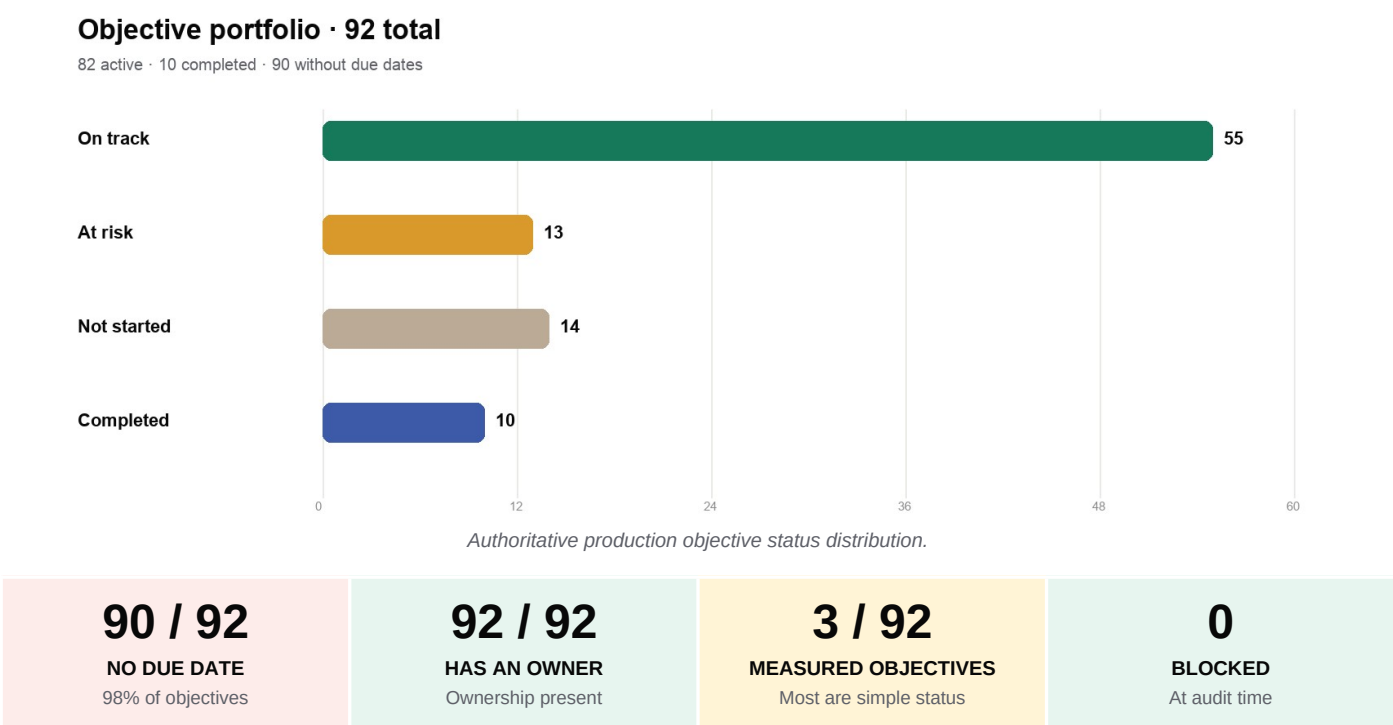

What the settled views show

Dashboard: 82 active — 55 on track, 13 at risk, 14 not started — plus 10 completed.

OKR: August check-in progress states 0 of 90 lines updated; four company OKRs are visible, followed by department lines.

KPI Command Center: 75% operating health, 82 active objectives, 80% NCR closure, 4 of 5 computed KPIs measured.

Objective execution health is 86%, above its 85% target, but the due-readiness KPI is green at 0 because 90 objectives have no due dates.

Manual scorecards have no data; production has 0 KPI definitions and 0 stored KPI datapoints.

The KPI 'OKR Trust' lens reports no key results even though the OKR workspace contains monthly lines; the two surfaces use different semantics or wiring.

OMP

Tasks & ProjectsOKRNCROrganization

+ New📄🌙🔔RARelease Smoke Admin
executive

OKR

Aug: 0 of 90 lines updated — 90 still open


Edit viewPresentation view+ Add main OKR

OKR LINE · 2026	STATUS	YTD AVG	CADENCE	DEPARTMENT	AUDIT FORM	BASELINE	TARGET	JAN	FEB	MAR
COMPANY 4 lines										
2.0 Digital Operating System Company · Company OKR · Jake Feil	On Track	23.1	Monthly	Company	Y	Not Active	FULL ACTIVE	10	15	2
Employee Cost of under 27% Company · Company OKR · Jake Feil	At Risk	25.9	Monthly	Company	N	36%	<27%	38	41	3
Greater Net Profit of 15% Company · Company OKR · Jake Feil	At Risk	5.8	Monthly	Company	N	10%	15%	6	-12	1
Zero TRIR Company · Company OKR · Jake Feil	On Track	0	Monthly	Company	N	0	0	0	0	0
CP WAREHOUSE 5 lines										
CP Stored Client SMI- Idle time. CP Warehouse · Department OKR · Kelby Kraft	On Track	0	Monthly	CP Warehouse	N	Define what success ...	1	.	.	.
CP Warehouse asset throughput per day- Create baseline CP Warehouse · Department OKR · Kelby Kraft	On Track	3.4	Monthly	CP Warehouse	N	Define what success ...	1	.	.	.
Decreasing the number of Events identifying RFID function issues. CP Warehouse · Department OKR · Kelby Kraft	On Track	24.4	Monthly	CP Warehouse	Y	Define what success ...	1	.	.	.
Meeting 100% of client stock level readiness CP Warehouse · Department OKR · Kelby Kraft	On Track	2.9	Monthly	CP Warehouse	Y	Define what success ...	1	.	.	.
Top (5) Routers - Time start to time										

Settled desktop OKR view. Four company OKRs and department lines are present after hydration.

Green can be technically correct and operationally misleading

The KPI layer is useful once hydrated, but several readings depend on absent source data.

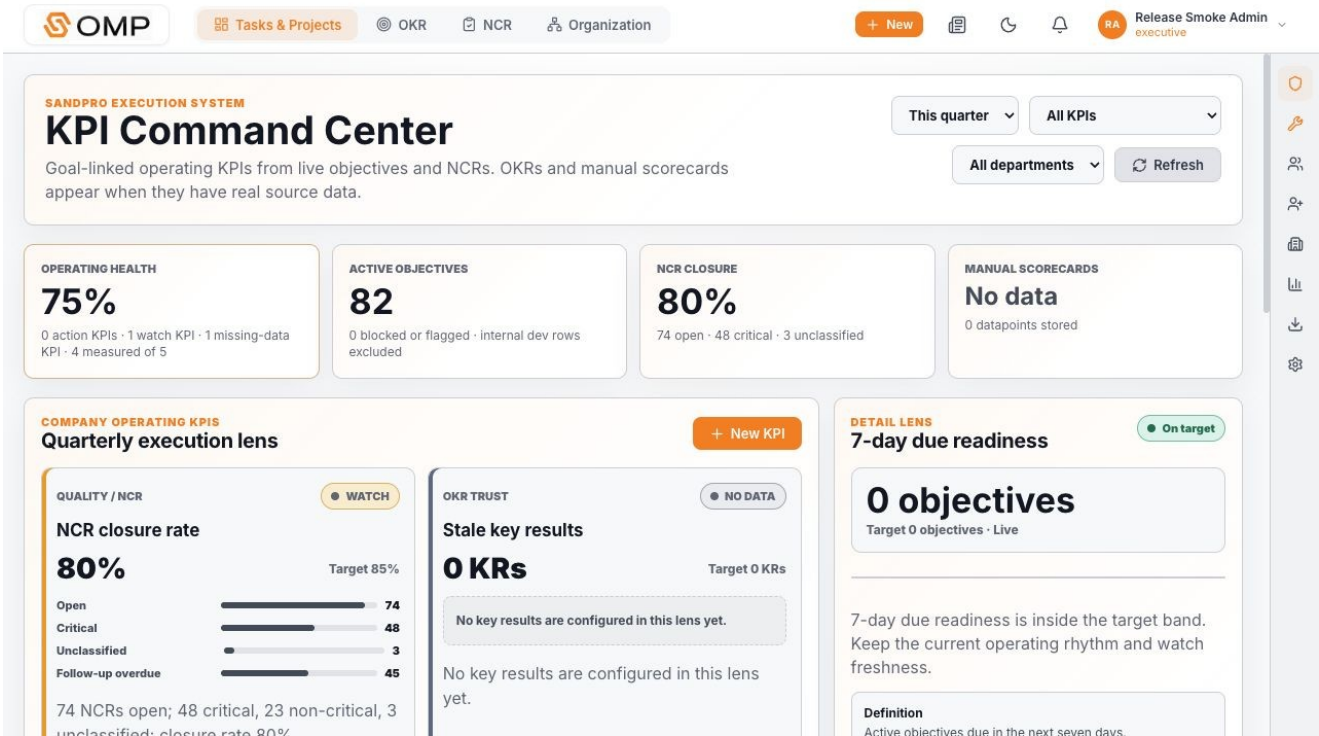

Settled KPI Command Center: 75% health, 82 active objectives, 80% NCR closure, manual scorecards absent.

KPI	OBSERVED	INTERPRETATION
Operating health	75%	One watch KPI and one missing-data KPI; 4 of 5 measured.
Objective execution	86%	58 active customer-visible objectives; 8 at-risk actions in the KPI lens.
7-day due readiness	On target · 0	Not evidence of schedule health when 90/92 objectives have no due date.
NCR closure	80% vs 85% target	296 of 370 closed; 74 remain open.
OKR Trust	No data · 0 stale KR	Does not reflect the populated OKR monthly-line workspace.
Manual scorecards	No data	No definitions or datapoints stored.

Keep in mind


For the first week, present due-readiness and OKR Trust as data-quality indicators, not performance grades. A green zero is not proof that time-bound execution is under control.

The application can surface the backlog; the organization cannot yet govern it

This is an operating-model risk more than a rendering problem.

NCR closeout readiness

296 closed · 74 open · all open rows need data

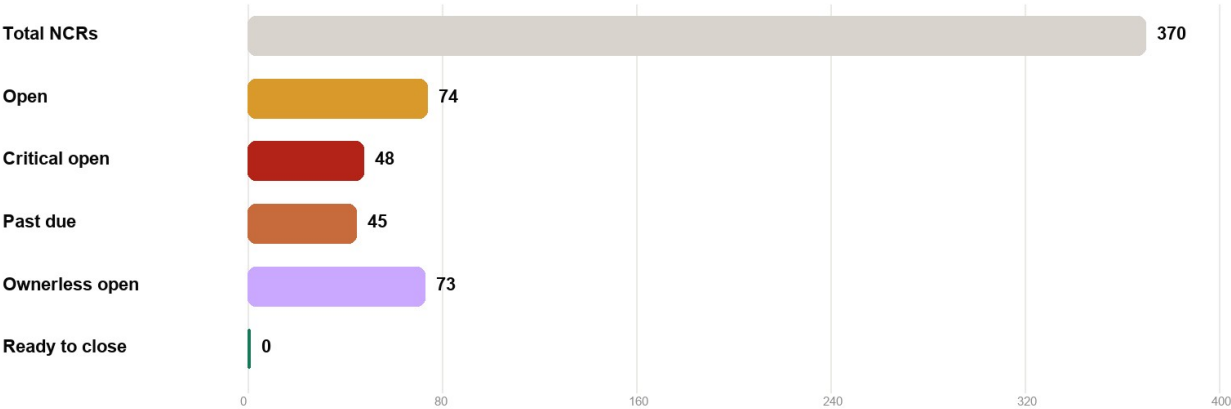

Authoritative database counts, reconciled against settled Tracker, Closeout, and Analytics views.

MEASURE	CURRENT	MEANING
Status	72 open · 2 in progress · 296 closed	74 work-in-scope records remain open.
Lifecycle	63 draft · 11 submitted · 296 closed	Most open NCRs have not moved beyond draft.
Critical open	48	65% of the open backlog is critical.
Past due	45	Past-due follow-up dates.
Older than 45 days	74	Database query; UI Trend Watch displayed 73.
Open without owner	73	Only one open NCR has an owner.
Open without due date	29	Follow-up cannot be schedule-managed.
Missing main department	194	Legacy department triage remains unresolved.
Closeout ready	0	All 74 open rows need data.
Supporting rows	0 actions · 0 attachments · 0 signatures	Structured closeout evidence tables are empty.

OMP

Tasks & ProjectsOKRNCROrganization

+ New📄🌙🔔RARelease Smoke Admin
executive

NCR Tracker

Non-conformance reports, root causes, corrective actions, and assigned follow-up work.

+ New NCR

Tracker

Closeout Report

Analytics

KPA Import

Dept triage (194)

Using the NCR Tracker

Filter by group, status, event type, or criticality to review open non-conformance reports.

Use Closeout Report to enter review data and close NCRs without round-tripping through Excel.

Create an objective when an NCR needs assigned action items before closeout.

74

OPEN

Click to filter

45

PAST DUE

Click to filter

0

DUE 7 DAYS

Click to filter

48

CRITICAL OPEN

Click to filter

296

CLOSED

Click to filter

Search NCRs...

Open (any stage)

All Groups

All Event Types

All Criticality

All Worksites

All Attention Levels

FROM

mm/dd/yyyy

TO

mm/dd/yyyy

Showing 72 of 370 NCRs

What do these filters mean?

Export visible list

REPORT	GROUP	TYPE	CRITICALITY	FOLLOW-UPS	STATUS
--------	-------	------	-------------	------------	--------

NCR #83849904

Submitted

Substandard Condition

Field techs, the yard - 46d overdue

OBSERVER

Aidyn Ross

PRIMARY GROUP AFFECTED

Shop

INTERNAL/EXTERNAL

Internal

NPT

No

Field Key ?

Settled NCR Tracker. Cards show 74 open, 45 past due, 48 critical open, 296 closed; the default list shows 72 status=open records.

PAGE 14

10 / NCR OPERATING PLAN

Do not turn backlog cleanup into tomorrow's launch task


Make the backlog visible, owned, and intentionally sequenced.

Launch-day minimum

- Name one NCR data steward and one executive escalation owner before the first cohort.
- Explain the count definitions: the card's 74 includes open plus in-progress; the default table displays 72 status=open records.
- Do not promise that all historical NCRs are clean. State that 194 require legacy department triage and 74 need closeout data.
- Freeze KPA imports and bulk department mapping during onboarding unless a named data steward is running a rehearsed procedure.
- Escalate the 48 critical open NCRs into a separate review cadence; do not bury them in the general rollout checklist.

First 30 days

WINDOW	ACTION	EXIT EVIDENCE
Day 1–2	Assign triage owner/group to every open NCR	74/74 have an accountable contact
Week 1	Resolve the 29 missing due dates and reconcile 73 vs 74 age count	Date rules documented; dashboard reconciled
Week 1–2	Triage 48 critical open NCRs	Executive-reviewed disposition and next date
Week 2–4	Map 194 legacy departments	No unresolved legacy mapping in current operating view
Month 1	Populate action, attachment, and signature evidence	Closeout-ready count begins moving above zero

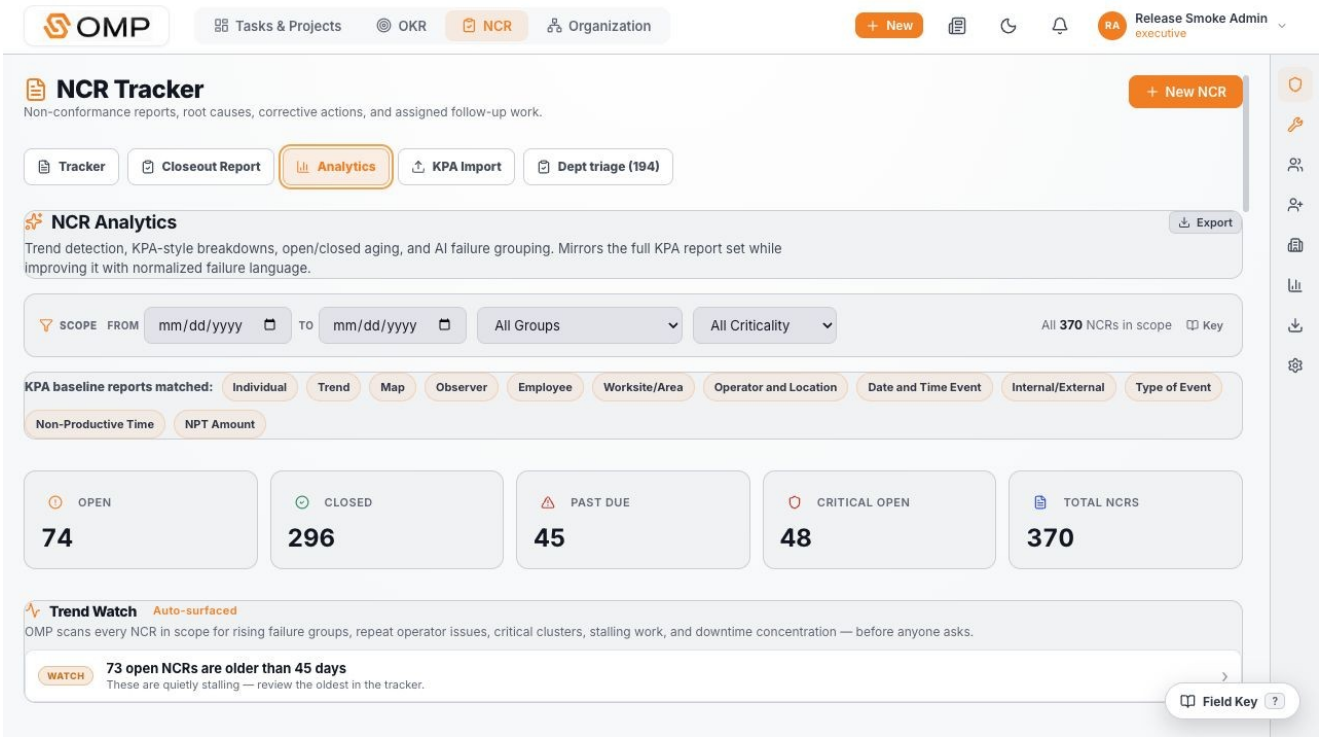

NCR Analytics is a strong production surface. It clearly exposes aging and criticality once loaded.


11 / NOTIFICATIONS

The infrastructure works for a pilot; company-wide reach does not

Channel readiness is constrained by preferences, sign-in, and device subscription — not by a visible failure spike.

Notification reach is opt-in constrained

Channel-enabled SandPro personnel out of 90

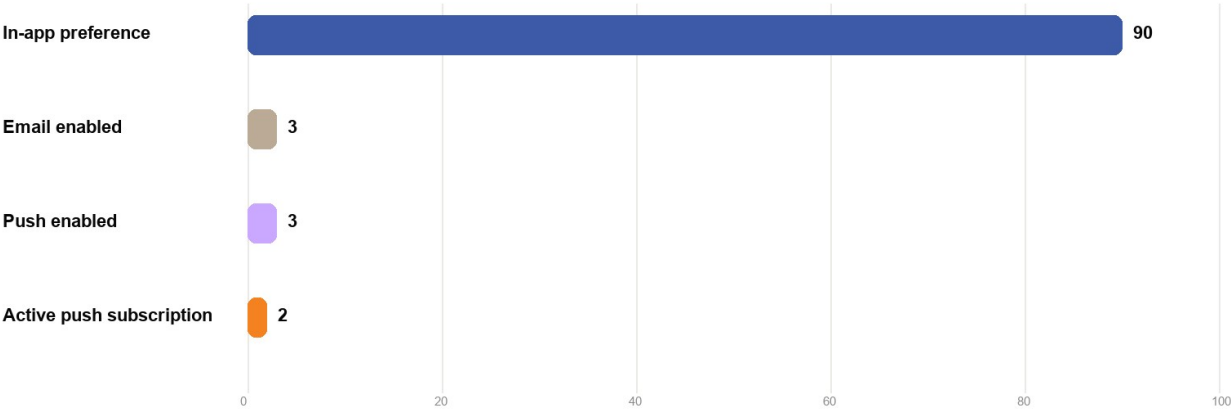

SandPro personnel notification coverage. 'Enabled' is a preference row; active push subscription is the stronger device-level signal.


SIGNAL	OBSERVED	INTERPRETATION
In-app enabled	90 / 90 personnel	Useful only after employees sign in.
Email enabled	3 / 90 personnel	Not a company-wide delivery channel yet.
Push enabled	3 / 90 personnel	Preference exists for three personnel.
Active push subscription	2 / 90 personnel	Only two SandPro personnel have an active device subscription.
Daily digest frequency	67 personnel	Frequency is set, but only three personnel have email enabled.
Past 24h email	4 sent · 0 failed	Positive infrastructure signal for the opted-in cohort.
Past 24h push	6 sent · 35 skipped by preference	No delivery failures in the sampled channel log; reach remains low.

Do not do tomorrow

- Do not send a blanket company-wide message and assume it reached all 90 employees.
- Do not treat 'daily digest' as enabled email delivery when the email channel itself is disabled.
- Do not enable push on employee devices without the employee present and without verifying the notification click target.
- Do not rely on the Release Smoke Admin's empty personal notification feed as proof that the system has no notifications.

Responsive behavior is credible; installed-device proof is still missing

Browser viewport evidence is useful, but it is not iPhone or Android installation evidence.

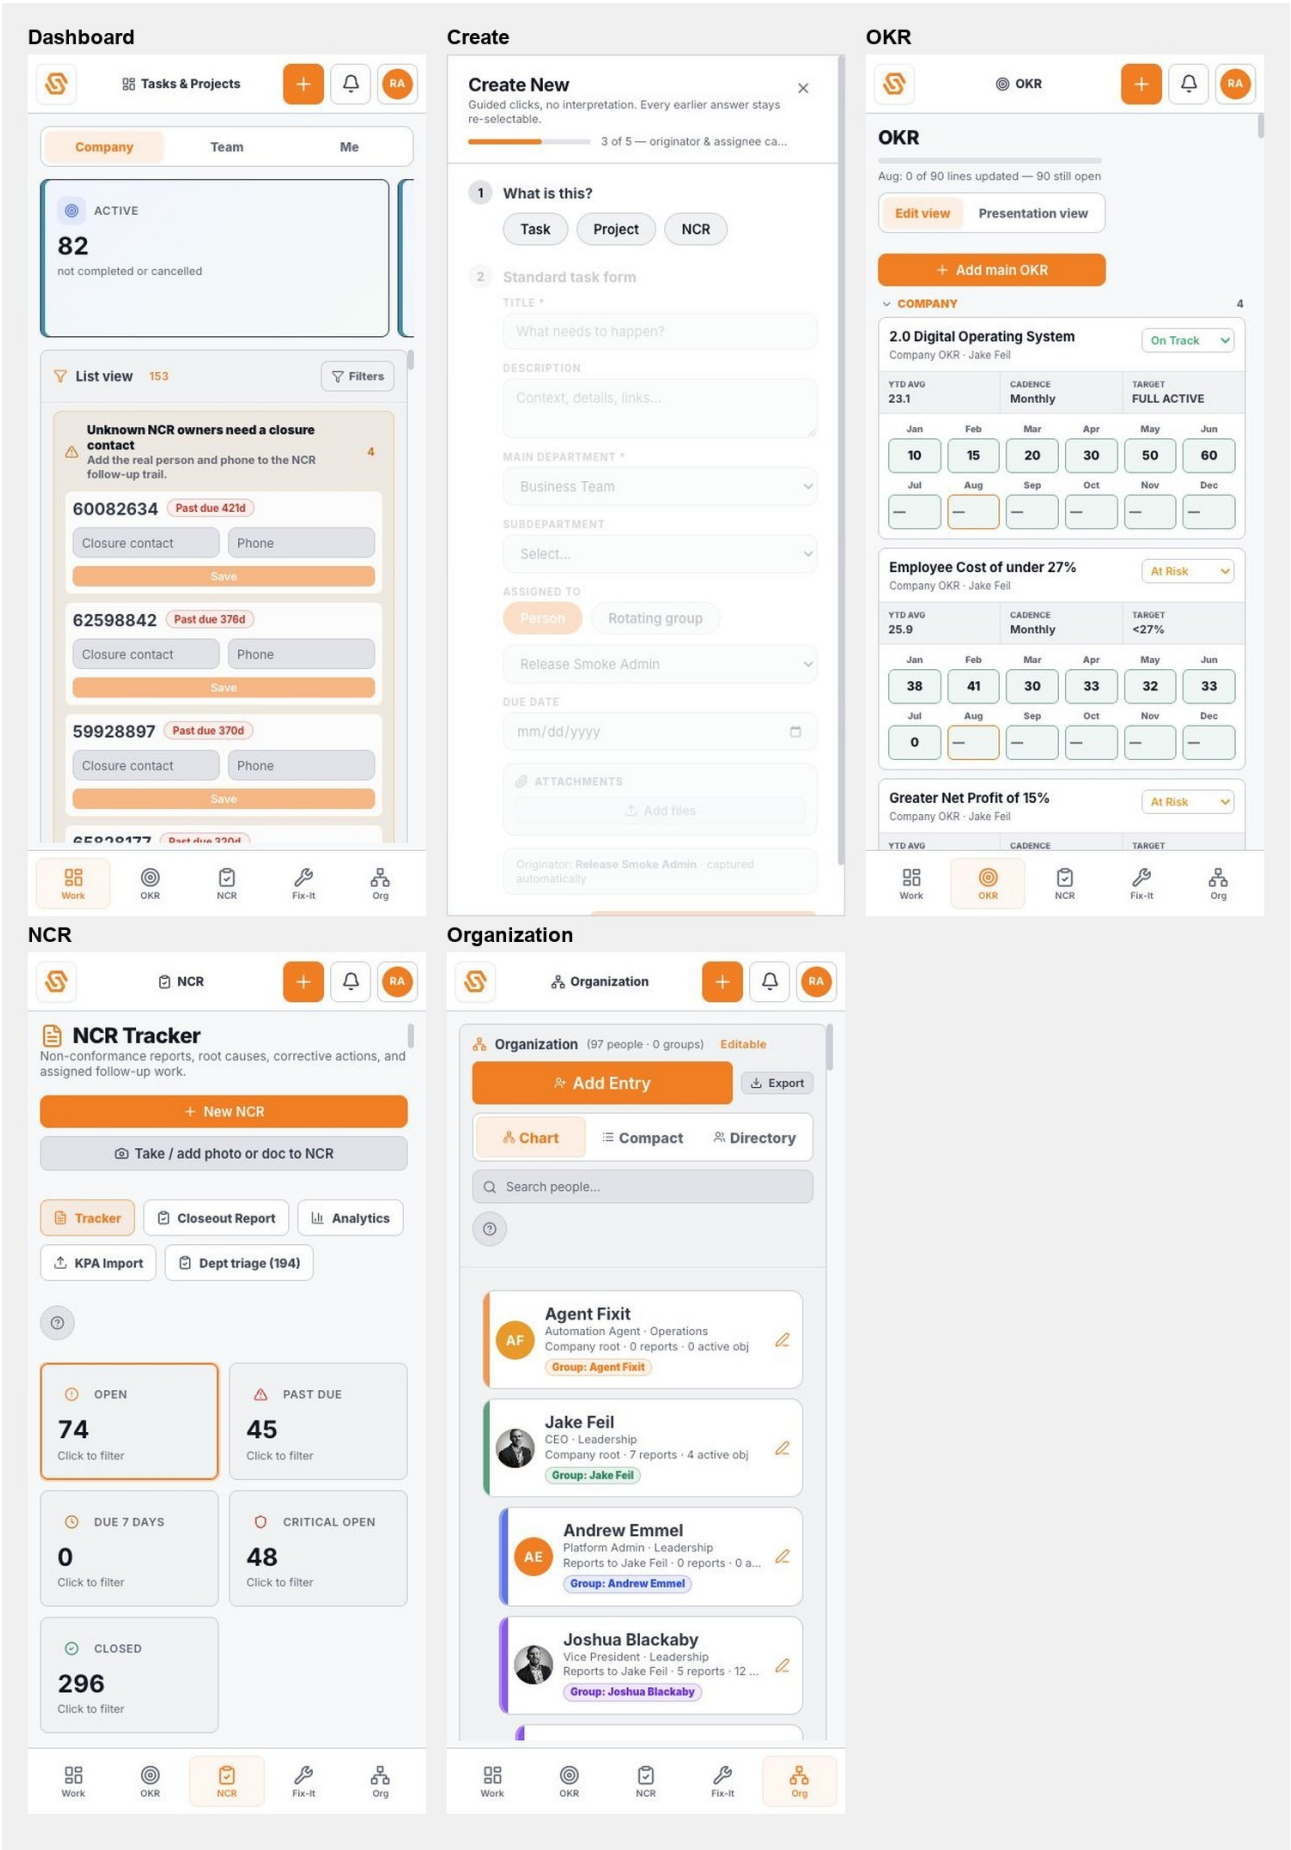

Observed at 390x844 after hydration. The mobile header, bottom navigation, Create, OKR, NCR, and Organization surfaces reflow coherently.

What passed

No major horizontal crop was observed at 390×844 across the five core surfaces.

Bottom navigation exposes Work, OKR, NCR, Fix-It, and Org with recognizable labels.

The Create wizard opens and remains usable at mobile width; no record was submitted.

The live manifest declares standalone display, portrait-primary orientation, maskable icons, start URL, and four shortcuts.

The live service worker is reachable, network-first for navigation, bypasses Supabase/API requests, and includes push click handling.

What remains unproven

Actual install, launch, icon, safe-area behavior, offline shell, and update adoption on a physical iPhone or Android device.

A real employee push permission prompt, active device subscription, notification arrival, and deep-link open.

PWA cache/version match after tomorrow's rollout; the shell currently identifies cache version sandpro-omp-shell-v10.

The false-zero window on slower cellular or field conditions; the 7.36-second result came from the in-app browser environment.

13 / SECURITY + PLATFORM

No active incident signal, but several release-hardening gaps remain

Security advisors are warnings, not proof of compromise. They still deserve explicit ownership before broad access.

Security findings

PRIORITY	FINDING	WHY IT MATTERS
P0 / ACCEPT OR FIX	handle_new_user() is SECURITY DEFINER and executable by anon and authenticated roles	Advisor-confirmed; direct privilege query confirmed both grants. The function is a trigger function, which limits ordinary RPC use, but the exposed grant is unnecessary attack surface.
P1	Leaked-password protection is disabled	Broad rollout increases the value of preventing known-compromised passwords.
P1	Five functions have mutable search_path	Harden function search paths to reduce object-resolution risk.
P1	Observed response lacks CSP and common hardening headers	HSTS is present; no CSP, X-Content-Type-Options, Referrer-Policy, Permissions-Policy, or frame restriction was observed on the root response.
P2	172 performance advisories	76 unindexed foreign keys, 56 auth RLS init-plan warnings, 22 multiple-permissive-policy warnings, 17 unused indexes, and one auth DB connection advisory.

Positive platform signals

- Strict-Transport-Security is present with a two-year max-age.
- Relevant public tables inspected have RLS enabled.
- Vercel reports the production deployment READY and returned no error/warning log rows for the prior 24 hours.
- The live static shell and service worker are cache hits at the edge, reducing asset delivery load.

Advisor references

- [Supabase function search_path lint](#)
- [Anonymous SECURITY DEFINER execution lint](#)
- [Authenticated SECURITY DEFINER execution lint](#)
- [Supabase leaked-password protection](#)


The roster and assignment groups exist; production hygiene needs one pass

Admin capacity is present, but QA identities are visible inside employee-facing organization surfaces.

97	0	10	129
PEOPLE DISPLAYED	ORG HEADER GROUPS	ASSIGNMENT GROUPS	GROUP MEMBERSHIPS
Includes 7 support / QA	Different from assignment groups	All active	Across 10 groups

Production hygiene findings

- Seven support/QA identities are present in the 97-person production roster: Agent Fixit, Andrew Emmel, Mobile Zero-Day QA, Release Smoke Admin, Release Smoke Member, SandPro QA Agent, and Thrawn NDAI.
- The mobile org chart presents Agent Fixit as a company root before the CEO and exposes platform/support identities to employees.
- The Organization header says 0 groups while the Admin assignment-group panel has 10 active groups. These are different concepts, but the labeling will look contradictory to new administrators.
- A completed objective titled 'Test' remains in production; a second objective containing 'test failures' appears to be legitimate operational wording and should not be removed blindly.
- All Personnel and Office Personnel are provisioned; the All Personnel group is the appropriate rollout audience only after activation/channel proof is complete.

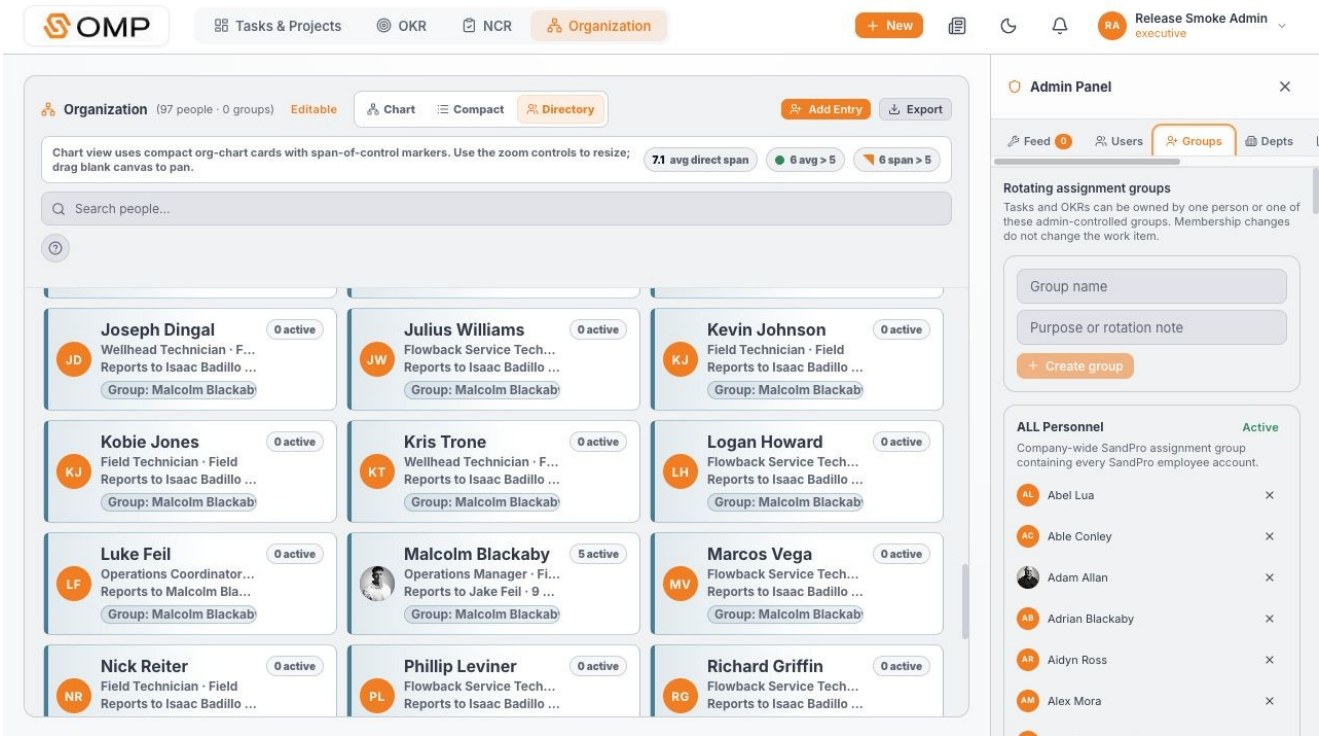

Admin assignment groups: 10 active groups, including All Personnel and Office Personnel.

15 / UX + ACCESSIBILITY

A cohesive light interface with a few high-leverage trust and keyboard gaps

The visual system is consistent across desktop and mobile; the findings below are about behavior and access, not style preference.

PRIORITY	FINDING	EVIDENCE / IMPACT
P0	False-empty loading states	Zero and 'no data' screens persist for 5–8 seconds before production values appear.
P0	Stale auto-open Daily	Launch date is June 24 on August 4.
P1	Clickable cards lack button semantics	Desktop KPI cards use cursor-pointer divs with no role/tab stop; keyboard users may not reach drilldowns.
P1	Profile trigger lacks button semantics	Clickable profile container is a div without role, tabIndex, or aria-expanded.
P1	Count-definition ambiguity	Dashboard Past Due objective KPI is 0 while the combined list has 45 past-due NCRs; NCR card shows 74 while default table shows 72.
P1	Create step indicator starts at 3 of 5	The first visible question is step 1 while the progress note says originator/assignee are captured; explain or simplify during onboarding.
P2	Organization group labeling	0 groups in Organization vs 10 assignment groups in Admin reads as contradictory.

Visual strengths

- Clear information hierarchy, restrained SandPro orange, readable cards, and consistent navigation.
- Responsive mobile header and bottom navigation preserve the five core surfaces without major crop.
- NCR Analytics and Closeout make the quality backlog legible and actionable once hydrated.
- Create uses a guided form with re-selectable type choices and clear department/assignment structure.
- Admin Users, Groups, Departments, Reports, Export, and Settings form a coherent operational rail.

Create New

Guided clicks, no interpretation. Every earlier answer stays re-selectable.

3 of 5 — originator & assignee captured for you

1

What is this?

Task

Project

NCR

2

Standard task form

TITLE *

What needs to happen?

DESCRIPTION

Context, details, links...

MAIN DEPARTMENT *

Business Team

SUBDEPARTMENT

Select...

ASSIGNED TO

Person

Rotating group

Release Smoke Admin

DUE DATE

mm/dd/yyyy

ATTACHMENTS

Add files

Desktop Create wizard opened successfully; no production record was submitted.

16 / ROLLOUT RUNBOOK

A staffed, observable launch plan for August 5

Use this as the operating checklist, not as permission to skip the hard gates.

WHEN	OWNER	ACTION / PROOF
T-24 to T-2h	Launch commander	Confirm current deploy ID, fresh Daily, cohort roster, ordinary-user proof, support channel, and stop criteria.
T-2h	Activation lead	Verify first-wave credentials; run one real-user sign-in and password recovery if applicable.
T-90m	Platform owner	Open Dashboard, OKR, KPI, NCR, Org, Fix-It; wait for hydration; record settled counts.
T-60m	Comms owner	Receive a real employee email; inspect inbox and junk; verify sender/subject/links.
T-45m	Device owner	Install/launch PWA on employee device; enable push; receive and open one push.
T0	Facilitator	Activate 5–10 employees. Every person completes sign-in, navigation, and notification checklist.
T+15m	Launch commander	Hold/advance decision. Do not start the next cohort until all current users are green.
T+60m	Data steward	Check new records, ownership visibility, notifications, Fix-It, and unexpected permission gaps.
EOD	Executive owner	Publish adoption totals, incidents, deferred issues, and next-day cohort decision.

Stop-the-line criteria

More than 10% of the current cohort cannot sign in or recover access within 10 minutes.

Any ordinary employee sees administrator-only controls or data outside intended visibility.

A route remains falsely empty after 15 seconds and one hard refresh.

A notification opens the wrong record, fails on the employee device, or is sent to the wrong audience.

Repeated 5xx errors, a visible crash, or data writes that do not persist after reread.

Rollback posture

Stop adding cohorts. Keep the successful pilot group active. Preserve data, logs, and screenshots. Roll back a deployment only if a specific deployment defect is confirmed and the previous production artifact is known-good; adoption trouble alone is not a reason for a database rollback.

17 / ACCEPTANCE CHECKLIST

Go / no-go decision sheet

Every red item needs evidence or an accountable risk acceptance. A verbal 'should work' is not evidence.

	GATE	ACCOUNTABLE OWNER	REQUIRED EVIDENCE
☐	Daily bulletin reflects August 5 rollout or is intentionally suppressed	Comms owner	Screenshot + timestamp
☐	First-wave employee accounts sign in on their actual devices	Activation lead	Named cohort list
☐	Ordinary employee sees intended records and no admin-only surfaces	Product owner	Screen recording / screenshots
☐	False-zero behavior mitigated or facilitator protocol accepted	Platform owner	Loading proof or signed playbook
☐	Email reaches inbox or documented junk path	Comms owner	Mailbox screenshot / trace
☐	Push arrives and opens correct record on a real device	Device owner	Device video / screenshot
☐	SECURITY DEFINER grants and leaked-password setting fixed or accepted	Security owner	Advisor rerun / risk signoff
☐	NCR triage and escalation owners named	Quality owner	Owner list + cadence
☐	Production deploy ID and rollback artifact recorded	Launch commander	Deployment record
☐	Stop criteria and support channel communicated	Launch commander	Launch message

Decision record

DECISION	OWNER	TIME	CONDITIONS / ACCEPTED RISK
GO / HOLD	_____	_____	_____ _____
Next cohort	_____	_____	_____ _____
EOD status	_____	_____	_____ _____

Final recommendation

Hold the unguarded company-wide launch. If the hard gates are cleared, proceed with a controlled, staffed rollout in small waves and treat activation, first-load truth, and channel proof as the first day's primary success measures.

APPENDIX A

Evidence index and reconciliation notes

The report embeds representative screenshots; the full evidence set remains alongside the source builder in the audit folder.

EVIDENCE	OBSERVED STATE	USE IN DECISION
01-entry.jpg	Stale auto-open Daily	Communication gate
02-dashboard.jpg	Settled desktop dashboard	Objective and mixed-list snapshot
24-okr-settled.jpg	Populated OKR workspace	OKR availability / 90-line check-in
25-kpi-settled.jpg	Computed KPI view	Performance and semantic review
26-ncr-tracker-settled.jpg	Populated NCR tracker	Backlog counts / count definitions
05-ncr-closeout.jpg	0 ready, 74 need data	Closeout readiness
06-ncr-analytics.jpg	Trend Watch and aging	Quality operating risk
08-ncr-triage.jpg	194 legacy mappings	Data stewardship
13-admin-groups.jpg	10 active assignment groups	Audience readiness
22-fixit-settled.jpg	0 active, 28 archived	Support readiness
27-create-wizard.jpg	Create opened; no submit	Core workflow availability
mobile/02,03,04,07,06	Responsive core surfaces	Mobile-browser readiness

Reconciliation notes

- NCR 74 vs 72: the high-level card counts open plus in-progress; the default selected table shows 72 status=open rows.
- NCR age 73 vs 74: production Analytics displayed 73 older than 45 days; the read-only database query at 08:40 CDT returned all 74 open rows older than 45 days. Reconcile the date boundary and source logic.
- OKR 90 vs objectives 92: the OKR progress bar tracks 90 open lines; the objective table contains 92 total rows including 10 completed. All 92 have OKR linkage fields populated in the production data model.
- Organization 0 groups vs Admin 10 groups: the Organization header appears to count org-chart groups; Admin counts assignment groups. Label the concepts explicitly.
- Past Due 0 vs 45: dashboard KPI describes objective deadlines; the combined list filter includes NCR follow-up deadlines. The UI needs clearer scope labels.

APPENDIX B

Audit limitations and data handling

A comprehensive audit is strongest when its exclusions are explicit.

Not tested

Destructive or write workflows: create submission, objective/NCR updates, owner assignment, org edits, imports, exports, user changes, password changes, group changes, Fix-It posting, commenting, or archival.

A real SandPro employee session or ordinary-role credential; the visual audit used Release Smoke Admin.

Physical iPhone, iPad, or Android installation; offline behavior; background notification delivery; cellular performance.

Microsoft 365 tenant logs, inbox/junk placement, sender-domain authentication, or employee mailbox delivery.

Staging mutations, local release preflight, schema migration, build reproducibility, or deployment rollback execution.

Full API/Postgres log export: the connected log endpoint did not return those services; Vercel and sampled Auth logs were used instead.

Data handling

Read-only SQL was used for aggregate metrics and named support/activation verification.

Screenshots contain production names and business records; this report should remain internal to SandPro/NDAI until redacted.

No production secret, password, token, or service-role credential is included in the deliverable.

The working repository was already dirty; unrelated changes were preserved and no deploy was attempted.

Evidence standard

A visible screen, passing deployment status, table count, or absence of logs is never enough by itself. The rollout gates require the behavior to work for the intended ordinary employee, on the intended device, with the intended data and communication channel.
